Kenneth Riedemann 12414 Linden Lane Leawood, KS 66209

May 31, 2005

Linda Finger City of Lawrence P.O. Box 708 Lawrence, Ks, 66044

Re: 805 Ohio Annual Progress Report

UPR-5-9-94

Dear Ms. Finger:

Enclosed is an updated "Milestone of Renovation dated May 16, 2005. We are up to date with all of the milestone items with the exception of the tuck-pointing of the chimneys. The process has begun, but there are several chimneys and some remain to be completed. Since the final four milestones were extended by the City Commission on May 25, 2004, we have not moved forward with the only one which has been started but not completed, which is the garage construction. The current completion date is September 1, 2005. As you know, we have requested an additional extension of the remaining milestone items in a letter to you dated May 18, 2005.

Much of the work this past year has been in the "Owners" apartment, finishing the work on the two north parlors which was approved and done in the past two years, as well as some redecorating of the downstairs bedroom and bathrooms.

We currently have one apartment rented through June 30, 2005 and the tenant would like to renew for another year. We also have one other apartment being utilized by a family friend on a very short term, non-rental basis. We expect to rent another apartment or two once the current extension request is approved.

While the Staff Inspection is normally in January, we can arrange it anytime if you will contact me and give me some dates which would work for you.

Please let me know if there is any additional information you need at this time. I look forward to hearing from you.

Sincerely,

/s/ Kenneth Riedemann

Kenneth Riedemann 12414 Linden Lane Leawood, KS 66209

May 18, 2005

Linda Finger City of Lawrence P.O. Box 708 Lawrence, Ks 66044

Re: 805 Ohio Street - UPR-5-9-94

Dear Ms. Finger:

On May 25, 2004 the City Commission of Lawrence approved the Staff Recommendation that the remaining final four Milestones be extended for one year from the Last Permitted Date to complete those items. The extension was given in order to allow us a one year period to request approval of the adaptive reuse of 805 Ohio under the proposed new zoning codes. In that the City Commission has not as yet adopted the new development and zoning codes, I hereby respectfully request that the City Commission grant another extension of the time to complete the four remaining Milestones. Please see Exhibit A, dated May 16, 2005, for the four remaining Milestones to be completed.

I hereby request that a two year extension be granted for the following Milestone items:

96-108.1	Garage construction complete	to	9.01.07
96-108.2	Phase out third apartment		9.01.07
108-120.1	Phase out apartments completely	to	9.01.08
108-120.1	Restore ballroom attic, remove parking	to	9.01.08

In addition, I would like to request that one already phased out apartment be allowed to be rented again, until 9.01.08, which will be the final phase out of the apartments.

Enclosed you will find Exhibit A, as well as the full submission that I made to you on May 17, 2004, which has some additional historical information and justification for this request for an extension.

Please let me know what additional information you need at this time, and when we might be able to have this request presented to the City Commission.

Sincerela

Kenneth Riedemann

Activity	AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current Date - Original Current Date - Original Current Date - Original Current Milestone List Status Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore entry hall Restore entry hall Restore entry hall Install asphalt driveway and parking(SW comer) Complete demo. of basement, ballroom attic. Complete four second floor apartments Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Restoration of four parlors UNDERWAY Phase out one apartment Current Milestone List Milestone List Status COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.97 COMPLETE 9.01.97 COMPLETE Ext. woodwork replacement, restoration & paint Restoration of four parlors UNDERWAY Phase out one apartment Current Current Current Milestone List Status COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE Ext. woodwork replacement, ballroom attic. 9.01.97 COMPLETE Ext. woodwork replacement, restoration & paint 9.01.97 COMPLETE Ext. woodwork replacement, restoration & paint 9.01.98 COMPLETE Ext. woodwork replacement, proch completely restored 9.01.99 COMPLETE Small southerly back porch completely restored 9.01.00 UNDERWAY 9.01.01 COMPLETE Small southerly back porch completely restored 9.01.01 COMPLETE Small southerly back porch completely 9.01.01 COMPLETE Small southerly back porch completely 9.01.02 COMPLETE Small southerly southerly southerly 9.01.03 COMPLETE Small southerly 9.01.03 COMPLETE 9.01.03 COMPLETE 9.01.04 Phase out one apartment 9.01.05 OMPLETE 9.01.05 OMPLETE	date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Date - Original Current TTEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. klitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Restore brick sideway and parking(SW comer) Complete demo. of basement, balliroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Front porch renovation of four parlors UNDERWAY Restoration of four parlors UNDERWAY Phase out one apartment Garage reconstruction UNDERWAY Phase out one apartment Garage construction COMPLETE Garage construction Completely Phase out one apartment COMPLETE Garage constr	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current Frems ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Replace roof Restore brick sidewalk Restore brick sidewalk Restore entry hall Restore entry hall Restore entry hall Complete demo. of basement, ballroom attic. Complete four second floor apartments Complete four second floor apartments Priori porch renovation UNDERWAY Replace marble floor in breezeway Froundation of four parlors UNDERWAY Restoration of four parlors UNDERWAY Phase out one apartment Complete ty restoration UNDERWAY Phase out of apartment CURRENT DATE Garage construction COMPLETE Garage construction COMPLETE Generale restoration COMPLETE Garage construction Completely Phase out on a partment Garage construction Completely Garage	
date for the original milestone schedule. Last Permitted Date - Original Current Milestone List Status Renovate 1st FIr. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore brick sidewalk Restore entry hall Complete demo. of basement, ballroom attlic. Complete four second floor apartments Complete four second floor apartments Restoration of four parlors UNDERWAY Poundation drain tile(French drain) installed Small southerly back porch Chimneys re-built Restoration of four parlors COMPLETE Chimneys re-built Restoration of four parlors COMPLETE Complete generonstruction UNDERWAY Phase out second apartment Garage construction COMPLETE Garage construction Completely Phase out of apartment GARAGE COMPLETE Garage construction COMPLETE Garage construction COMPLETE Garage construction Completely Phase out of apartment Garage construction Completely Phase out of apartment Garage construction Completely Phase out of apartment Garage construction Completely Garage construction Completely Garage construction	AND, therefore, the commencement date for the original milestone Last Permitted Date - Original Current Milestone List Status Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Restore entry hall Complete demo. of basement, ballroom attic. Complete four second floor apartment Replace marble floor in breezeway Foundation of rain tile(French drain) installed Small southerly back porch completely restored Complete reconstruction UNDERWAY Phase out one apartment CURRENT DATE Garage construction COMPLETE Garage construction COMPLETE COMPLETE COMPLETE Status Last Permitted Date - Original Last Permitted Last Permitted Date - Original Last Permitted Date - Original Last Permitted Date - Original Cumplete Situs Status Status Status COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE 0.01.96 COMPLETE 0.01.96 COMPLETE 0.01.97 COMPLETE 0.01.97 COMPLETE 0.01.97 COMPLETE 0.01.98 COMPLETE 0.01.99 COMPLETE 0.01.01 COMPLETE 0.01.01 COMPLETE 0.01.01 COMPLETE 0.01.01 COMPLETE 0.01.01 COMPLETE 0.01.01 COMPLETE 0.01.02 COMPLETE 0.01.01 COMPLETE 0.01.01 COMPLETE 0.01.02 COMPLETE 0.01.01 COMPLETE 0.01.01 COMPLETE 0.01.02 COMPLETE 0.01.01 COMPLETE 0.01.02 COMPLETE 0.01.03 COMPLETE 0.01.03 COMPLETE 0.01.01 COMPLETE 0.01.03 COMPLETE 0.01.01 COMPLETE 0.01.01 COMPLETE 0.01.02 COMPLETE 0.01.03 COMPLETE 0.01.03 COMPLETE 0.01.03 COMPLETE 0.01.04 Phase out of apartment 0.01.04 Phase out of apartment 0.01.05	date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st FIr. kitchen, bathroom, bedroom Restore brick sidewalk Restore entry hall Replace marble floor in brezzeway Front porch renovation UNDERWAY Replace marble floor in brezzeway Front porch restoration of four parlors UNDERWAY Restoration of four parlors UNDERWAY Phase out one apartment Garage construction COMPLETE Garage construction COMPLETE Garage reconstruction COMPLETE Garage as a completely Phase out of apartment COMPLETE Garage construction COMPLETE Garage as completely Phase out of apartment COMPLETE Garage construction COMPLETE Garage as completely 9.01.03 COMPLETE Garage construction COMPLETE Garage construction COMPLETE Garage construction Completely Phase out of apartment COMPLETE Garage construction COMPLETE Garage construction COMPLETE Garage construction COMPLETE Garage construction Completely Phase out of apartment COMPLETE Garage construction Completely Phase out of apartment COMPLETE Garage construction Completely 9.01.03 COMPLETE Garage construction Completely 9.01.04 Phase out of apartment COMPLETE Garage construction Completely 9.01.04 Phase out of apartment COMPLETE 9.01.05	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone Last Permitted Schedule. Date - Original Current TTEMS ON ORIGINAL MILESTONE LIST Milestone List Status Status Renovate 1st Fir. kitchen, bathroom, bedroom 3.01.96 COMPLETE Restore brick sidewalk Replace roof 3.01.96 COMPLETE Restore entry half Complete demo. of basement, ballroom attic. 9.01.96 COMPLETE Install asphalt driveway and parking(SW comer) 9.01.96 COMPLETE Complete demo. of basement, ballroom attic. 9.01.96 COMPLETE Complete demo. of basement, ballroom attic. 9.01.96 COMPLETE Replace marble floor in breezeway 9.01.97 COMPLETE Complete back porch 9.01.97 COMPLETE Replace marble floor in breezeway 9.01.97 COMPLETE Replace marble floor in breezeway 9.01.97 COMPLETE Replace marble floor in breezeway 9.01.97 COMPLETE Front porch renovation UNDERWAY 9.01.97 COMPLETE Replacement, parlors UNDERWAY 9.01.97 COMPLETE Replacement, parlors UNDERWAY 9.01.97 COMPLETE Restoration of four parlors COMPLETE 9.01.98 COMPLETE Chimneys re-built 9.01.99 COMPLETE Chimneys re-built 9.01.00 UNDERWAY 9.01.01 COMPLETE Chimneys re-built 9.01.01 COMPLETE Complete parlors COMPLETE 9.01.02 UNDERWAY 9.01.02 UNDERWAY 9.01.02 UNDERWAY 9.01.03 COMPLETE COMPLETE 9.01.03 COMPLETE COMPLETE 9.01.03 COMPLETE COMPLETE 9.01.03 COMPLETE 0.01.04 Phase out one apartment 9.01.04 Phase out one apartment 9.01.05 COMPLETE 9.01.04 Phase out of apartment 9.01.05 COMPLETE 9.01.05	96
schedule. Last Permitted Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, balliroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Foundation drain file(French drain) installed Small southerly back porch completely restored Chimneys re-built Chimneys re-built Restoration of four parlors COMPLETE Restoration of four parlors COMPLETE Restoration of parlors COMPLETE Restoration of parlors COMPLETE Restoration of parlors COMPLETE Restoration of four parlors COMPLETE Restoration of four parlors COMPLETE Restoration of parlors COMPLETE Restoration of Jour parlors COMPLETE Restoration of Jour parlors COMPLETE Restoration of Cour parlors COMPLETE Chimneys re-built Complete Source Storation UNDERWAY Phase out one apartment CURRENT DATE Garage construction COMPLETE Complete Source Storation COMPLETE COMPLETE Garage construction COMPLETE Garage construction COMPLETE COMPLETE COMPLETE Source Source Storation COMPLETE Source Sourc	AND, therefore, the commencement date for the original milestone Last Permitted Date - Original Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore brick sidewalk Restore entry hall Complete four second floor apartments Complete four second floor apartments Replace marble floor in breezeway Replace marble floor in breezeway Replacement, restoration & paint Restoration of four parlors UNDERWAY Foundation drain tile(French drain) installed Small southerly back porch completely restored Chimneys re-built Restoration of four parlors COMPLETE Restoration of four parlors UNDERWAY Phase out one apartment Garage reconstruction UNDERWAY Phase out second apartment Garage construction COMPLETE Garage construction COMPLETE Garage construction COMPLETE Garage construction COMPLETE Garage out third apartment Garage construction COMPLETE 9,01,04	Idate of first multi-family occupancy, ANID, therefore, the commencement date for the original milestone Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Milestone List Status	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone Last Permitted	90
schedule. Last Permitted Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, balliroom attic. Complete four second floor apartments Replace marble floor in breezeway Foundation drain title(French drain) installed Restoration of four parlors COMPLETE Small southerly back porch completely restored Completely restored Complete Southerly Southerly Southerly Southerly Restoration UNDERWAY Phase out one apartment CURRENT DATE COMPLETE COMPLETE Southerly Southerly COMPLETE COMPLETE Southerly Southerly COMPLETE COMPLETE Southerly COMPLETE Southerly Sout	AND, therefore, the commencement date for the original milestone Last Permitted Schedule. Last Permitted Date - Original Current Status Renovate 1st FIr. kitchen, bathroom, bedroom Paint two car garage Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Foundation drain tile(French drain) installed Restoration of four parlors UNDERWAY Foundation and brick restoration UNDERWAY Phase out one apartment CURRENT DATE COMPLETE Restoration of four parlors COMPLETE COMPLETE Restoration of four parlors COMPLETE Restoration of four parlors COMPLETE Small southerly back porch completely restored Chimneys re-built Garage reconstruction UNDERWAY Phase out one apartment CURRENT DATE COMPLETE COMPLETE School-tring and brick restoration COMPLETE CURRENT DATE COMPLETE COMPLETE School-tring and brick restoration COMPLETE COMPLETE School-tring and brick restoration COMPLETE COMPLETE School-tring and brick restoration COMPLETE COMPLETE COMPLETE COMPLETE School-tring and brick restoration COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE School-tring and brick restoration COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE School-tring and brick restoration COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE School-tring and brick restoration COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE School-tring and brick restoration COMPLETE	date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom A.01.96 Replace roof Restore brick sidewalk Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW comer) Complete demo. of basement, balliroom attic. Complete four second floor apartments Peront porch renovation UNDERWAY Front porch renovation UNDERWAY Restoration of four parlors UNDERWAY Small southerly back porch completely restored Chimneys re-built Tuck-pointing and brick restoration UNDERWAY Phase out one apartment CURRENT DATE Garage construction COMPLETE Phase out second apartment GURRENT DATE Garage construction COMPLETE GOMPLETE GOMPLET	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Milestone List Status Stat	5
schedule. Schedule. Last Permitted Date - Original Current Date - Original Current Milestone List Status Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Restoration of four parlors UNDERWAY Restoration of four parlors UNDERWAY Completer Seps to front porch with wood Restoration of four parlors COMPLETE Foundation drain tile(French drain) installed Chimneys re-built Restoration of four parlors COMPLETE Completer Seps to front porch with wood Restoration of four parlors COMPLETE Completer 9.01.99 COMPLETE Completer 9.01.99 COMPLETE Ext. woodwork replacement, restoration & paint Repl.concrete steps to front porch with wood Restoration of four parlors UNDERWAY COMPLETE Completer 9.01.99 COMPLETE Completer 9.01.00 COMPLETE Completer 9.01.01 COMPLETE Restoration of four parlors COMPLETE Restoration of four parlors COMPLETE Completer 9.01.01 COMPLETE Restoration of four parlors COMPLETE Complete 9.01.01 COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE Shall southerly back porch completely restored 9.01.01 COMPLETE Shall asphale demo. of the completely restored COMPLETE	AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Date - Original Date - Original Current Milestone List Status Renovate 1st Fir. kitchen, bathroom, bedroom Paint two car garage Resider only hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Complete four second floor apartments Complete four second floor apartments Complete back porch Replace marble floor in breezeway Proundation drain tile(French drain) installed Restoration of four parlors UNDERWAY Chimneys re-built Restoration of four parlors COMPLETE Restoration of four parlors COMPLETE Chimneys re-built Restoration of four parlors COMPLETE Restoration of four parlors COMPLETE Chimneys re-built Restoration of four parlors COMPLETE Restoration of four parlors COMPLETE Restoration of four parlors COMPLETE Chimneys re-built Restoration of four parlors COMPLETE Restoration of four parlors COMPLETE Chimneys re-built Restoration of four parlors COMPLETE Restoration of four parlors COMPLETE Complete go.01.02 COMPLETE COMPLETE COMPLETE OMPLETE Somall southerly back porch completely restored 9.01.09 COMPLETE COMPLETE COMPLETE OMPLETE COMPLETE OMPLETE COMPLETE COMPLETE OMPLETE COMPLETE COMPLETE OMPLETE COMPLETE OMPLETE COMPLETE OMPLETE COMPLETE COMPLETE OMPLETE COMPLETE COMPLETE COMPLETE COMPLETE OMPLETE COMPLETE COMPLET	date of first multi-family occupancy, AND, therefore, the commencement	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone Schedule. Date - Original Date - Original Date - Original Date - Original Complete Renovate 1st Fir. kitchen, bathroom, bedroom 3.01.96 COMPLETE Paint two car garage Replace roof Restoration of four parlors UNDERWAY Phase out second apartment Date - Original Date - Original Complete Complete Extra Milestone List Status AND, therefore, the commencement Date - Original Date - Original Complete Complete Complete Status Status AND, therefore, the commencement Date - Original Date - Original Date - Original Complete Complete Status Status AND, therefore, the commencement Date - Original Complete Complete Status Status AND, therefore, the commencement Sol 1.96 COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.97 COMPLETE COMPLETE Poundation of four parlors UNDERWAY Phase out one apartment Tuck-pointing and brick restoration UNDERWAY Phase out second apartment Tuck-pointing and brick restoration COMPLETE 9.01.03 COMPLETE 9.01.03 COMPLETE 9.01.03 COMPLETE 9.01.03 COMPLETE 9.01.03 COMPLETE 9.01.03 COMPLETE COMPLETE 9.01.03 COMPLETE 9.01.03 COMPLETE COMPLETE 9.01.03 COMPLETE 9.01.03 COMPLETE COMPLETE 9.01.03 COMPLETE OMPLETE OMPL	5
date for the original milestone schedule. Last Permitted Date - Original Date - Original Current Milestone List Status Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Restoration of four parlors UNDERWAY Restoration of four parlors UNDERWAY Restoration of four parlors COMPLETE Chimneys re-built Restoration of four parlors COMPLETE Complete reconstruction UNDERWAY Phase out one apartment Schedule. Last Permitted Date - Original Current Milestone List Status Milestone List Status Milestone List Status COMPLETE 3.01.96 COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.97 COMPLETE COMPLETE COMPLETE Parlors Complete with wood 9.01.98 COMPLETE COMPLETE 9.01.99 COMPLETE COMPLETE Parlors COMPLETE Complete steps to front porch with wood 9.01.99 COMPLETE COMPLETE COMPLETE Complete construction UNDERWAY 9.01.01 COMPLETE COMPLETE Complete construction UNDERWAY 9.01.02 COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE OMPLETE COMPLETE	AND, therefore, the commencement date for the original milestone Last Permitted Date - Original Current Date - Original Current Milestone List Status Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Replace roof Restore brick sidewalk Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete four second floor apartments Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Restoration of four parlors UNDERWAY Restoration of four parlors UNDERWAY Restoration of four parlors COMPLETE Small southerly back porch completely restored Chimneys re-built Restoration of four parlors COMPLETE Restoration of four parlors COMPLETE Complete four second completely restored Chimneys re-built Restoration of four parlors COMPLETE Restoration of four parlors COMPLETE Complete four sectoration UNDERWAY Don 1.02 COMPLETE COMPLETE Small southerly back porch completely restored Chimneys re-built Restoration of four parlors COMPLETE Restoration of four parlors COMPLETE Complete four parlors COMPLETE Restoration of four parlors COMPLETE Complete four parlors COMPLETE Restoration of four parlors COMPLETE Complete four parlors COMPLETE Complete four parlors COMPLETE COMPL	date of first multi-family occupancy, AND, therefore, the commencement Last Permitted Date - Original Current Status	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone Schedule. Last Permitted Date - Original Date - Original Current Milestone List Status Renovate 1st Fir. kitchen, bathroom, bedroom Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Replace marble floor in breezeway Front porch renovation UNDERWAY Repliconcrete steps to front porch with wood Restoration of four parlors UNDERWAY Restoration of four parlors UNDERWAY Restoration of four parlors COMPLETE Restoration of parlors COMPLETE Restoration of four parlors COMPLETE Schedule. COMPLETE Garage reconstruction UNDERWAY 9,01.02 COMPLETE	
date for the original milestone schedule. Last Permitted Date - Original Current Milestone List Status Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Restoration of four parlors UNDERWAY Phase out one apartment CompleteTE Restoration of four parlors COMPLETE Restoration of four parlors COMPLETE CompleteTE CompleteTE Restoration of four parlors COMPLETE Restoration of four parlors COMPLETE CompleteTE Restoration of four parlors COMPLETE Restoration of four parlors COMPLETE CompleteTE CompleteTE CompleteTE Restoration of four parlors COMPLETE CompleteTE CompleteTE CompleteTE CompleteTE Restoration of four parlors COMPLETE CompleteTE CompleteT	AND, therefore, the commencement date for the original milestone Last Permitted Date - Original Current Milestone List Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Restoration of four parlors UNDERWAY Small southerly back porch completely restored Chimneys re-built Garage reconstruction UNDERWAY Phase out one apartment AND, therefore, the comment test original Last Permitted Date - Original Current Milestone List Milestone List Milestone List Status COMPLETE 3.01.96 COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.97 COMPLETE COMPLETE 9.01.97 COMPLETE COMPLETE Ext. woodwork replacement, restoration & paint Repl.concrete steps to front porch with wood 9.01.98 COMPLETE Ext. woodwork replacement, restoration & paint 9.01.98 COMPLETE COMPLETE Complete four parlors UNDERWAY 9.01.01 COMPLETE COMPLETE OCMPLETE COMPLETE Complete four parlors COMPLETE OCMPLETE Complete four parlors COMPLETE OCMPLETE COMPLETE COMPLETE COMPLETE COMPLETE OCMPLETE COMPLETE COMPLE	date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone Last Permitted Date - Original Current Date - Original Current Milestone List Status	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Date - Original Date - Original Date - Original Current Milestone List Renovate 1st Fir. kitchen, bathroom, bedroom Paint two car garage Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Complete four second floor apartments Replace marble floor in breezeway Replace marble floor in breezeway Replace marble floor front porch with wood Repliconcrete steps to front porch with wood Restoration of four parlors UNDERWAY Foundation drain tile(French drain) installed Chimneys re-built Restoration of four parlors COMPLETE Complete Teconstruction UNDERWAY Phase out one apartment OMPLETE COMPLETE SCOMPLETE COMPLETE COMPLETE SCOMPLETE SCOMPLETE COMPLETE SOMPLETE COMPLETE SOMPLETE SOMPLETE COMPLETE SOMPLETE SOMPLETE COMPLETE COMPLETE COMPLETE COMPLETE SOMPLETE COMPLETE COMPLETE SOMPLETE COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE SOMPLETE COMPLETE COM	
date for the original milestone Schedule. Last Permitted	AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Date - Original Current Milestone List Status Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore brick sidewalk Restore entry hall Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Restoration of four parlors UNDERWAY Restoration of four parlors COMPLETE Restoration of four parlors COMPLETE Restoration of four parlors COMPLETE Restoration UNDERWAY Tuck-pointing and brick restoration UNDERWAY Garage reconstruction UNDERWAY Garage reconstruction UNDERWAY Garage reconstruction UNDERWAY Dot.00 Last Permitted CumpleTE Alast Permitted CompleTE ComPLETE COMPLETE COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.97 COMPLETE Replace marble floor in breezeway 9.01.97 COMPLETE Replace marble floor in breezeway 9.01.97 COMPLETE Replace marble floor in breezeway 9.01.98 COMPLETE Replace marble floor in breezeway 9.01.99 COMPLETE COMPLETE Replace marble floor in breezeway 9.01.99 COMPLETE Replace marble floor in breezeway 9.01.99 COMPLETE COMPLETE Replace marble floor in breezeway 9.01.99 COMPLETE COMPLETE Restoration of four parlors UNDERWAY 9.01.99 COMPLETE	date of first multi-family occupancy,	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Date - Original Last Permitted Last Permitted Date - Original Current Milestone List Status Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete four second floor apartments Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Restoration of four parlors UNDERWAY Tuck-pointing and brick restoration UNDERWAY Garage reconstruction UNDERWAY Tuck-pointing and brick restoration UNDERWAY Garage reconstruction UNDERWAY OMPLETE OMPLETE OCMPLETE Somall southerly back porch completely restored Complete E Complete four parlors COMPLETE Complete Steps to front porch with wood 9.01.09 COMPLETE COMPLETE Small southerly back porch completely restored Chimneys re-built Restoration of four parlors COMPLETE COMPLETE COMPLETE COMPLETE Small southerly back porch completely restored Chimneys re-built Restoration of four parlors COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE Small southerly back porch completely restored COMPLETE C	
date for the original milestone Schedule. Last Permitted	AND, therefore, the commencement date for the original milestone Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Restoration of four parlors UNDERWAY Restoration of four parlors UNDERWAY Restoration four parlors UNDERWAY Restoration drain tile(French drain) installed Small southerly back porch completely restored Complete Et Complete 9.01.01 COMPLETE COMPLETE Restoration of four parlors COMPLETE Complete steps to front porch with wood Small southerly back porch completely restored Complete Small southerly back porch completely restored Complete Small southerly back porch completely restored Complete Steps to foor underway Tuck-pointing and brick restoration underway Tuck-pointing a	date of first multi-family occupancy,	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Date - Original Current Date - Original Current Milestone List Status Renovate 1st Fir. kitchen, bathroom, bedroom Renovate 1st Fir. kitchen, bathroom, bedroom Restore brick sidewalk Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Replacement, restoration & paint Replacement, restoration & paint Replacement four parlors UNDERWAY Restoration of four parlors UNDERWAY Restoration of four parlors UNDERWAY COMPLETE Foundation drain tile(French drain) installed Small southerly back porch completely restored Chimneys re-built Tuck-pointing and brick restoration UNDERWAY OUNDERWAY Tuck-pointing and brick restoration UNDERWAY Restoration of four parlors COMPLETE OMPLETE COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE Small southerly back porch completely restored Quilon QUNDERWAY OUNDERWAY OUNDERWAY Tuck-pointing and brick restoration UNDERWAY OUNDERWAY Tuck-pointing and brick restoration UNDERWAY OUNDERWAY Tuck-pointing and brick restoration UNDERWAY OUNDERWAY OUNDERWAY	
date for the original milestone Schedule.	AND, therefore, the commencement date for the original milestone chedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Replace roof Restore brick sidewalk Restore entry hall Restore four second floor apartments Complete four second floor apartments Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Repl. concrete steps to front porch with wood Restoration of four parlors UNDERWAY Foundation drain tile(French drain) installed Small southerly back porch completely restored COMPLETE COMPLETE Restoration of OUNDERWAY Tuck-pointing and brick restoration UNDERWAY Date - Original Current Milestone List Milestone List Status COMPLETE And Current Milestone List Status COMPLETE And Current Milestone List Status COMPLETE C	date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone Last Permitted Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st FIr. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Restoration of four parlors UNDERWAY Restoration of four parlors UNDERWAY Foundation drain tile(French drain) installed Small southerly back porch completely restored COMPLETE ROMPLETE ROMP	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current Paint two car garage Replace roof Restore brick sidewalk Restore brick sidewalk Restore brick sidewalk Restore brick sidewaly and parking(SW corner) Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Restoration of four parlors UNDERWAY Restoration of four parlors UNDERWAY Foundation drain tile(French drain) installed Small southerly back porch completely restored COMPLETE COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.97 COMPLETE 9.01.98 COMPLETE 9.01.99 COMPLETE Restoration of four parlors UNDERWAY 9.01.99 COMPLETE Restoration drain tile(French drain) installed Small southerly back porch completely restored 9.01.00 UNDERWAY OUNDERWAY	
date for the original milestone Schedule.	AND, therefore, the commencement date for the original milestone schedule. Date - Original Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Restore demo. of basement, ballroom attic. Complete four second floor apartments Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Reploconcrete steps to front porch with wood Restoration of four parlors UNDERWAY Foundation drain tile(French drain) installed Chimneys re-built Current Date - Original Current Date - Original Current Milestone List Status COMPLETE All Status All Status COMPLETE All Status All Status All Status COMPLETE South List Status COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE COMPLETE Paint two car garage 3.01.96 COMPLETE 9.01.96 COMPLETE COMPLETE COMPLETE Paint two car garage 3.01.96 COMPLETE 9.01.96 COMPLETE COMPLETE COMPLETE COMPLETE Paint two car garage 3.01.96 COMPLETE 9.01.98 COMPLETE COMPLETE Restoration of four parlors UNDERWAY 9.01.99 COMPLETE	date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Date - Original Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Restore entry hall Restore four second floor apartments Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Repl.concrete steps to front porch with wood Restoration of four parlors UNDERWAY Foundation drain tile(French drain) installed Chimneys re-built AND, therefore, the comment tast Permitted Last Permitted Date - Original Current Milestone List Status COMPLETE And 196 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.97 COMPLETE COMPLETE Replace marble floor in breezeway 9.01.97 COMPLETE Replace marble floor in breezeway 9.01.98 COMPLETE COMPLETE COMPLETE Replace marble floor in breezeway 9.01.98 COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE OMPLETE COMPLETE	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Date - Original Date - Original Date - Original Current Milestone List Frems on Original milestone Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore brick sidewalk Restore entry hall Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Restoration of four parlors UNDERWAY Restoration of four parlors UNDERWAY Foundation drain tile(French drain) installed Chimneys re-built NAMILESTONE LIST Milestone List Status Milestone List Milestone List Status COMPLETE COMPLETE COMPLETE GOMPLETE COMPLETE COMPLETE COMPLETE Restoration of four parlors UNDERWAY Foundation drain tile(French drain) installed Small southerly back porch completely restored 9,01.00 UNDERWAY UNDERWAY UNDERWAY	
date for the original milestone Last Permitted	AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Renovate back porch Restoration of four parlors UNDERWAY Foundation drain tile(French drain) installed Small southerly hack porch completely restored COMPLETE	AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Restore brick sidewalk Restore brick sidewalk Restore entry hall Restore entry hall Restore four second floor apartments Install asphalt driveway and parking(SW corner) Replace marble floor in breezeway Front porch renovation UNDERWAY Repl.concrete steps to front porch with wood Repl.concrete steps to front porch with wood Small southerly back porch COMPLETTE Restored 001.99 COMPLETTE Replace marble floor in breezeway Replace marble floor in breezeway Foundation of four parlors UNDERWAY Replacement, restoration & paint Repl.concrete steps to front porch with wood Small southerly back porch completely restored COMPLETTE Restored 001.09 COMPLETTE Replacement, restoration & paint Repl.concrete Steps to front porch with wood Small southerly back porch completely restored COMPLETTE Restored 001.00 COMPLETTE Replacement, restoration & paint Repl.concrete Steps to front porch with wood Small southerly back porch completely restored COMPLETTE	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Repl.concrete steps to front porch with wood Restoration of four parlors UNDERWAY Restoration of four parlors UNDERWAY Foundation drain tile(French drain) installed Small southerly back porch COMPLETE COMPLETE COMPLETE COMPLETE Restoration of four parlors UNDERWAY 9.01.97 COMPLETE C	
date for the original milestone Schedule.	AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Repl. concrete steps to front porch with wood Restoration of four parlors UNDERWAY Foundation of four parlors UNDERWAY Foundation of fain tile(French drain) installed COMPLETE COMPLETE COMPLETE Restoration of four parlors UNDERWAY Foundation of fain tile(French drain) installed COMPLETE	date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Flr. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Repl. concrete steps to front porch with wood Restoration of four parlors UNDERWAY Foundation drain tile/French drain) installed AND, therefore, the comment and the comm	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Paint two car garage Restore brick sidewalk Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Replace marble flour is breezeway Front porch renovation UNDERWAY Restoration of four parlors UNDERWAY Restoration of four parlors UNDERWAY Restoration drain tile/French drain) installed Restore date of first multi-family occupancy, AND, therefore, the comment and the date of first multi-family occupancy, AND, therefore, the comment and the date of first multi-family occupancy, AND, therefore, the comment and the comme	
date for the original milestone Schedule. Last Permitted	AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Date - Original Current Milestone List Status Renovate 1st Flr. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Repl. concrete steps to front porch with wood Repl.	date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Repl.concrete steps to front porch with wood Repl.concrete steps to front porch with wood Repl.concrete steps to front porch with wood ROMPLETE ROMPLETE Repl.concrete steps to front porch with wood ROMPLETE ROMPLETE COMPLETE COMPLETE ROMPLETE COMPLETE	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone Schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Restore entry hall Restore entry hall Restore four second floor apartments Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Repl.concrete steps to front porch with wood Repl.concrete steps to front porch with wood COMPLETE COMP	
date for the original milestone Schedule.	AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current Date - Original Current Milestone List Status Renovate 1st Flr. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore brick sidewalk Restore brick sidewalk Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Front porches to store the foot to see huith wood Renovate back porch Ext. woodwork replacement, restoration & paint Ont one contact store to front porch with wood COMPLETE	date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current Frent porch sidewalk Replace marble floor in breezeway Front porch states to front porch with word AND, therefore, the commencement AND, therefore, the commencement Last Permitted Date - Original Current Milestone List Milestone List Status COMPLETE 3.01.96 COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.97 COMPLETE COMPLETE Pent two car garable floor in breezeway Front porch states to front porch with word COMPLETE Replacement, restoration & paint Part to COMPLETE	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Renovate back porch Renovate back porch Ext. woodwork replacement, restoration & paint Renovate to the foot to och with wood Renovate back porch COMPLETE Ext. woodwork replacement, restoration & paint SOME TETE COMPLETE	
date for the original milestone Schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Flr. kitchen, bathroom, bedroom Paint two car garage Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Renovate back porch Last Permitted Current Milestone List Status 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.97 COMPLETE COMPLETE Renovate back porch Renovate back porch	AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Date - Original Current Milestone List Status Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Renovate back porch COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.97 COMPLETE 9.01.97 COMPLETE 9.01.97 COMPLETE 9.01.97 COMPLETE 9.01.97 COMPLETE COMPLETE Paint two car garage COMPLETE 9.01.96 COMPLETE COMPLETE COMPLETE Paint two car garage 3.01.96 COMPLETE 9.01.96 COMPLETE	date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current Milestone List Front porch renovation UNDERWAY AND, therefore, the commencement Last Permitted Date - Original Current Milestone List Status AND, therefore, the commencement Last Permitted Date - Original Current Milestone List Status COMPLETE 3.01.96 COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone Schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Renovate back porch	
date for the original milestone Schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Last Permitted Current Milestone List Status 3.01.96 COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE	AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Date - Original Current Milestone List Status Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Alst Permitted Date - Original Current Milestone List Status COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE Replace marble floor in breezeway Front porch renovation UNDERWAY 9.01.97 COMPLETE	date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current Milestone List Status Renovate 1st Fir. kitchen, bathroom, bedroom Paint two car garage Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY AND, therefore in the comment attic. Last Permitted Date - Original Current Milestone List Status COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.97 COMPLETE COMPLETE COMPLETE COMPLETE Replace marble floor in breezeway Front porch renovation UNDERWAY 9.01.97 COMPLETE	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone Schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Front porch renovation UNDERWAY Note: September 1, 1995 was the date of the comment of the complete	
date for the original milestone schedule. Last Permitted Date - Original Current Milestone List Status Renovate 1st Flr. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete four second floor apartments Replace marble floor in breezeway Replace marble floor in breezeway Last Permitted Date - Original Current Milestone List Status 3.01.96 COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE COMPLETE 9.01.96 COMPLETE COMPLETE COMPLETE COMPLETE	AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current Paint two car garage Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete four second floor apartments Replace marble floor in breezeway AND, therefore, the commencement ballroom attic. Last Permitted Date - Original Current Milestone List Status 3.01.96 COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE COMPLETE 9.01.96 COMPLETE	date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current Date - Original Current Milestone List Status Renovate 1st Flr. kitchen, bathroom, bedroom Paint two car garage Restore brick sidewalk Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway 9.01.96 COMPLETE COMPLETE COMPLETE Schedule. Last Permitted Current Milestone List Status 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE COMPLETE COMPLETE COMPLETE Schedule.	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone Schedule. ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments Replace marble floor in breezeway Note: September 1, 1995 was the Last Permitted Date - Original Current Milestone List Status Status 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE	
date for the original milestone control control control complete four second floor apartments control con	AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current Milestone List Renovate 1st Flr. kitchen, bathroom, bedroom Paint two car garage Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments AND, therefore, the commencement Last Permitted Date - Original Current Milestone List Status 3.01.96 COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE COMPLETE 9.01.96 COMPLETE COMPLETE COMPLETE OCOMPLETE COMPLETE OCOMPLETE COMPLETE COMPLETE COMPLETE 9.01.96 COMPLETE	date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Flr. kitchen, bathroom, bedroom Replace roof Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Complete four second floor apartments AND, therefore, the comment team of the comment of the complete of the comment of the comment of the comment of the complete of the comment of the comment of the complete of the comment of the comment of the comment of the complete of the comment of the	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Flr. kitchen, bathroom, bedroom Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete four second floor apartments Nites Paint two care garage Restore brick sidewalk Restore brick sidewalk Restore entry hall Complete four second floor apartments Other Items AND, therefore, the comment ballroom attic. Last Permitted Date - Original Current Milestone List Status COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE	
date for the original milestone Schedule. Last Permitted Date - Original Current Date - Original Current Milestone List Status Renovate 1st Flr. kitchen, bathroom, bedroom Paint two car garage Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Last Permitted Date - Original Current Milestone List Status 3.01.96 COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE	AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current Milestone List Status Renovate 1st Flr. kitchen, bathroom, bedroom Paint two car garage Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Aust Permitted Date - Original Current Milestone List Status 3.01.96 COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE	date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Flr. kitchen, bathroom, bedroom Paint two car garage Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. AND, therefore, the commencement Last Permitted Date - Original Current Milestone List Status 3.01.96 COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE COMPLETE	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Flr. kitchen, bathroom, bedroom Paint two car garage Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Complete demo. of basement, ballroom attic. Nate Permitted Last Permitted Current Milestone List Status 3.01.96 COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE COMPLETE	
date for the original milestone Schedule. Last Permitted Date - Original Current Milestone List Status Renovate 1st Flr. kitchen, bathroom, bedroom Paint two car garage Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Last Permitted Current Milestone List Status 3.01.96 COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE	AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current Milestone List Status Renovate 1st Flr. kitchen, bathroom, bedroom Paint two car garage Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) AND, therefore, the commencement Last Permitted Date - Original Current Milestone List Status 3.01.96 COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE	date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current Milestone List Status Renovate 1st Flr. kitchen, bathroom, bedroom Paint two car garage Replace roof Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) AND, therefore, the commencement Last Permitted Date - Original Current Milestone List Status 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current Milestone List Renovate 1st Flr. kitchen, bathroom, bedroom Paint two car garage Restore brick sidewalk Restore entry hall Install asphalt driveway and parking(SW corner) Note: September 1, 1995 was the Last Permitted Date - Original Current Milestone List Status 3.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE 9.01.96 COMPLETE	
date for the original milestone schedule. ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Paint two car garage Replace roof Restore brick sidewalk Restore entry hall Ast Permitted Date - Original Current Milestone List Status 3.01.96 COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE	AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current Milestone List Status Renovate 1st Fir. kitchen, bathroom, bedroom Paint two car garage Replace roof Restore brick sidewalk Restore entry hall AND, therefore, the commencement Last Permitted Date - Original Current Milestone List Status 3.01.96 COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE	date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Flr. kitchen, bathroom, bedroom Paint two car garage Restore brick sidewalk Restore entry hall AND, therefore, the commencement Last Permitted Date - Original Current Milestone List Status 3.01.96 COMPLETE 3.01.96 COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current Milestone List Renovate 1st Fir. kitchen, bathroom, bedroom Paint two car garage Replace roof Restore brick sidewalk Restore entry hall Note: September 1, 1995 was the Last Permitted Date - Original Current Milestone List Status 3.01.96 COMPLETE 3.01.96 COMPLETE 9.01.96 COMPLETE	100
date for the original milestone schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Flr. kitchen, bathroom, bedroom Paint two car garage Replace roof Restore brick sidewalk Ast Permitted Date - Original Current Milestone List Status 3.01.96 COMPLETE 3.01.96 COMPLETE 3.01.96 COMPLETE	AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Flr. kitchen, bathroom, bedroom Paint two car garage Replace roof Restore brick sidewalk AND, therefore, the commencement Last Permitted Date - Original Current Milestone List Status 3.01.96 COMPLETE 3.01.96 COMPLETE 3.01.96 COMPLETE	date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Paint two car garage Replace roof Restore brick sidewalk AND, therefore, the commencement Last Permitted Current Milestone List Status 3.01.96 COMPLETE 3.01.96 COMPLETE 3.01.96 COMPLETE	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Milestone List Renovate 1st Flr. kitchen, bathroom, bedroom Paint two car garage Replace roof Restore brick sidewalk OCMPLETE 3.01.96 COMPLETE 3.01.96 COMPLETE 3.01.96 COMPLETE	
date for the original milestone control contro	AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Paint two car garage Replace roof AND, therefore, the commencement Last Permitted Current Milestone List Status 3.01.96 COMPLETE 3.01.96 COMPLETE	date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Milestone List Renovate 1st Fir. kitchen, bathroom, bedroom Paint two car garage Replace roof Replace roof AND, therefore, the commencement Last Permitted Date - Original Current Milestone List Status 3.01.96 COMPLETE	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Paint two car garage Replace roof Note: September 1, 1995 was the Last Permitted Date - Original Current Milestone List Status 3.01.96 COMPLETE 3.01.96 COMPLETE	
date for the original milestone contract contra	AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Milestone List Status Paint two car garage 3.01.96 COMPLETE	date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Flr. kitchen, bathroom, bedroom Paint two car garage AND, therefore, the commencement Last Permitted Date - Original Current Milestone List Status 3.01.96 COMPLETE	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Milestone List Status Paint two car garage 3.01.96 COMPLETE	
date for the original milestone schedule. ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom Asst Permitted Date - Original Current Milestone List Status 3.01.96 COMPLETE	AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Milestone List Status Renovate 1st Fir. kitchen, bathroom, bedroom 3.01.96 COMPLETE	date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. Last Permitted Date - Original Current ITEMS ON ORIGINAL MILESTONE LIST Milestone List Status Renovate 1st Fir. kitchen, bathroom, bedroom 3.01.96 COMPLETE	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement date for the original milestone schedule. ITEMS ON ORIGINAL MILESTONE LIST Renovate 1st Fir. kitchen, bathroom, bedroom 3.01.96 COMPLETE	
ne original milestone Last Permitted Date - Original Current N ORIGINAL MILESTONE LIST Milestone List Status	refore, the commencement ne original milestone Last Permitted Date - Original Current N ORIGINAL MILESTONE LIST Milestone List Status	st multi-family occupancy, refore, the commencement ne original milestone Last Permitted Date - Original Current N ORIGINAL MILESTONE LIST Milestone List Status	st multi-family occupancy, refore, the commencement ne original milestone Last Permitted Date - Original Current Milestone List Status	1
ne original milestone Last Permitted Date - Original Current	refore, the commencement ne original milestone Last Permitted Date - Original Current	st multi-family occupancy, refore, the commencement ne original milestone Last Permitted Date - Original Current	st multi-family occupancy, refore, the commencement ne original milestone Last Permitted Date - Original Current	=
ne original milestone Last Permitted	refore, the commencement ne original milestone Last Permitted	st multi-family occupancy, refore, the commencement ne original milestone Last Permitted	st multi-family occupancy, refore, the commencement ne original milestone Last Permitted	D
	ement	ement	ancy, sement	on
	AND, therefore, the commencement	date of first multi-family occupancy, AND, therefore, the commencement	Note: September 1, 1995 was the date of first multi-family occupancy, AND, therefore, the commencement	ise
Note: September 1, 1995 was the date of first multi-family occupancy,	Note: September 1, 1995 was the	MILESTONES OF RENOVATION		

KENNETH RIEDEMANN 12414 LINDEN LANE LEAWOOD, KS 66209

May 17, 2004

Linda Finger City of Lawrence P.O. Box 708 Lawrence, KS 66044

Re: 805 Ohio Street - UPR-5-9-94

Dear Ms. Finger:

Please consider this presentation as our formal request to modify and to extend certain Milestone Requirements of UPR-5-9-94, which were revised pursuant to the letter dated April 6, 1999, which was signed by you. The summary of the current 'Milestones of Renovation' is included as Exhibit A.

We hereby request approval of the modifications and extensions that are set forth on the 'Requested Changes to Revised Milestones of Renovation – UPR-5-9-94', which is attached hereto as Exhibit B and made a part hereof. Each of the seven modifications and extensions are identified with a 'Discussion Point Number' from 1 through 7. The following is a discussion of the reasons for this request for each of the seven requests.

Discussion Points 1,2,4 and 5 are requests to extend the dates by which apartments are to be taken out of service. This is, of course, the essence of this request for an extension of the timeline of the UPR. Some of the reasons for the requests are outlined below.

1. We are now convinced now that the income earned from the rental of the four apartments is probably the best, if not the only way to help the ownership of 805 to continue to maintain this significant historical property in the manner in which everyone involved wants it to be maintained. 805 is a very expensive property to operate, especially in the area of utility costs, and the fact that it is on the outer edge of that part of Old West Lawrence area that contains the best of the old mansions, and 805

is surrounded by smaller multi-family properties, limits its desirability as a single-family residence.

- 2. During the late 1998 and early 1999 period we were required to make substantial and very costly modifications to the property in order to meet City standards to operate the property as a five dwelling unit property. As your files will show, we had to put in two new heating systems with smoke detectors and dampers in the systems, completely rewired the building, installed an alarm system with a pull station, installed a dropped ceiling throughout the basement, as well as many other very costly improvements. It has been five years since those improvements were completed, but we have not even come close to recovering the cost of making the improvements that were necessary to have the five dwelling units.
- 3. The property continues to work very well as an apartment property. Because of the nature of the property and the amount of rent that we have to charge, we have attracted very serious students and non-students as well. There is very adequate parking and to my knowledge there has never been an incident which has been disruptive to the neighborhood.
- 4. The Kansas State Historical Society has been very supportive concerning the current use of 805 and in a letter dated February 14, 2003, stated "Adaptive reuse and rehabilitation are valuable tools used to preserve historic buildings that might otherwise be lost to deterioration or inappropriate development." The letter is included herewith as Exhibit C.

Discussion Point 3 is about the completion date for the garage construction. The objective here is to make the garage more compatible with the design of 805. We need some additional time to think through the changes and have them put into a format that someone at the City can review and approve.

Discussion Point 6 is the restoration of the attic. The fire marshal has expressed concern on a couple of occasions that we would make use of the attic without proper fire and safety considerations being addressed. For that reason, when we reconfigured the layout of the single-family portion of the property and used the western portion of the second floor, we made the attic accessible only from within the single-family portion, and it is accessible only for maintenance purposes. The third floor cannot be used unless we sprinkle the entire building, and we do not intend to do so, therefore we will not be using the attic space for any purpose other than maintenance of the property. For those reasons, the Milestone of restoring the attic is no longer practical, and therefore, we are requesting that it be eliminated.

Discussion Point 7 is the tearing out of the resident parking spaces. We are requesting that this the City extend this Milestone in order to conform to the extension of the phasing out of the last apartment, which would be 9.01.11.

I am taking the liberty of including with this request two photographic examples of how historic properties in Des Moines, Iowa are being used commercially as office buildings in order to help the owners maintain them in the manner demanded by their architectural and historical significance. The Finkbine Mansion in particular resembles 805 Ohio, and is being used as a general office building for lawyers and other similar uses. I include this information to support my position that I feel that the best opportunity that we have to continue to maintain 805 Ohio in the manner that its architectural and historic significance demands, is to continue to allow the four apartments in addition to the "owner's residence", and to try to show that it is being done successfully in another community. The photos are included as Exhibits D and E.

I invite any one who is interested to contact me for a tour of 805 Ohio, and I thank you for your consideration of this request to extend UPR-5-9-94 as outlined herein.

Sincerely,

Kenneth Riedemann

	WILLIAM TO OTHORATION				
	MILES LONES OF RENOVALION				
	Note: September 1, 1995 was the				
	date of first multi-family occupancy,				
	AND, therefore, the commencement				
	date for the original milestone			Revised	
	schedule.	Last Permitted		Milestones	Notes and/or
		Date - Original	Current	Last Date	Proposed Revisions
	ITEMS ON ORIGINAL MILESTONE LIST	Milestone List	Status	Permitted	To Nature and Scope of Work
0-6.1	Renovate 1st Flr. kitchen, bathroom, bedroom	3.01.96	COMPLETE		
0-6.2	Paint two car garage	3.01.96	COMPLETE		
0-6.3	Replace roof	3.01.96	COMPLETE		
0-6.4	Restore brick sidewalk	3.01.96	COMPLETE		
6-12.1	Restore entry hall	9.01.96	COMPLETE		
6-12.2	Install asphalt driveway and parking(SW corner)	9.01.96	COMPLETE		
6-12.3	Complete demo. of basement, ballroom attic.	9.01.96	COMPLETE		
6-12.4	Complete four second floor apartments	9.01.96	COMPLETE		Changed to one 1st floor and 3 - 2nd floor apts.
12-24.1	Replace marble floor in breezeway	9.01.97	COMPLETE		Refinished wood floors as they originally were
12.24.2	Front porch renovation UNDERWAY	9.01.97	COMPLETE		
12-24.3	Renovate back porch	9.01.97	COMPLETE		
0-36.1	Ext. woodwork replacement, restoration & paint	9.01.98	COMPLETE		
0-36.2	Repl.concrete steps to front porch with wood	9.01.98	COMPLETE		
36-48.2	Restoration of four parlors UNDERWAY	9.01.99	COMPLETE		
36-48.2	Foundation drain tile(French drain) installed	9.01.99	COMPLETE		
48-60.1	Small southerly back porch completely restored	9.01.00	COMPLETE		
48-60.2	Chimneys re-built	9.01.00	UNDERWAY		Require tuckpointing only - Will begin summer 2004
60-72.1	Tuck-pointing and brick restoration UNDERWAY	9.01.01	COMPLETE		
60-72.2	Restoration of four parlors COMPLETE	9.01.01	COMPLETE		
72-84.1	Garage reconstruction UNDERWAY	9.01.02	UNDERWAY		Completion required by 9.01.04
72-84.2	Phase out one apartment	9.01.02	COMPLETE		Apartment off market.
84-96.1	Tuck-pointing and brick restoration COMPLETE	9.01.03	COMPLETE		
84-96.2	Phase out second apartment	9.01.03	COMPLETE		Apartment off market.
	CURRENT DATE				
96-108.1	Garage construction COMPLETE	9.01.04		9.01.04	
96-108.2	Phase out third apartment	9.01.04		9.01.04	
108-120.1	Phase out of apartments completely	9.01.05		9.01.05	
108-120.2	Restore ballroom attic, tear out parking.	9.01.05		9.01.05	
4.05.04					
					∧ TIGILX ¬

Requested Changes To Revised Milestones of Renovation
Item on Original
Milestone List
Phase out one apartment
Phase out second apartment
Garage construction COMPLETE
Phase out third apartment
Phase out apartments completely
Restore ballroom attic
Tear out parking



KANSAS

STATE

HISTORICAL

SOCIETY

Cultural Resources Division

6425 S.W. 6th Avenue Topeka, Kansas 66615-1099 PHONE# (785) 272-8681 FAX# (785) 272-8682 TTY# (785) 272-8683

KANSAS HISTORY CENTER

Administration
Center for Historical Research
Cultural Resources
Education / Outreach
Historic Sites
Kansas Museum of History
Library & Archives

HISTORIC SITES

Adair Cabin Constitution Hall Cottonwood Ranch First Territorial Capitol Fort Hays Goodnow House Grinter Place Hollenberg Station Kaw Mission Marais des Cygnes Massacre Mine Creek Battlefield Native American Heritage Museum Pawnee Indian Village Pawnee Rock Shawnee Indian Mission

February 14, 2003

KENNETH RIEDEMANN 12414 LINDEN LANE LEAWOOD KS 66209

RE: Rehabilitation and Adaptive Reuse of the Jacob House Residence at 805 Ohio in Lawrence, KS

Dear Mr. Riedemann:

The Kansas State Historic Preservation Office has determined that the building referenced above is a contributing element of the Old West Lawrence Historic District as listed on the National Register of Historic Places. As such, the building is eligible for the State Historic Rehabilitation Tax Credit program. This program was introduced in 2001 to help fund the rehabilitations and general maintenance of historic properties across Kansas.

You were one of the first applicants of the program. You proposed several items of work in December 2001 involving the property at 805 Ohio. The completed project was approved for purposes of the tax credit program in January 2002 because all work appeared to meet the Secretary of the Interior's *Standards for Rehabilitation*.

This project was known to be part of a general rehabilitation of the building involving a new use of the property for a purpose compatible with its historic use as a home. The overall historic character of the building has been retained and even enhanced by the removal of non-historic materials that had previously been applied inappropriately. The repair of historic elements such as wood floors, wood trim, and original plaster, according to appropriate guidelines, further enhances this rehabilitation project.


Adaptive reuse and rehabilitation are valuable tools used to preserve historic buildings that might otherwise be lost to deterioration or inappropriate development. Projects that follow the *Standards* in this way should be encouraged.

If you have any questions about this project, please contact Katrina Klingaman at 785-272-8681 ext. 226 or kklingaman@kshs.org.


Sincerely,

Richard Pankratz, Director Cultural Resources Division


805 OHIO
Apartment 2 – Studio
Second Floor North

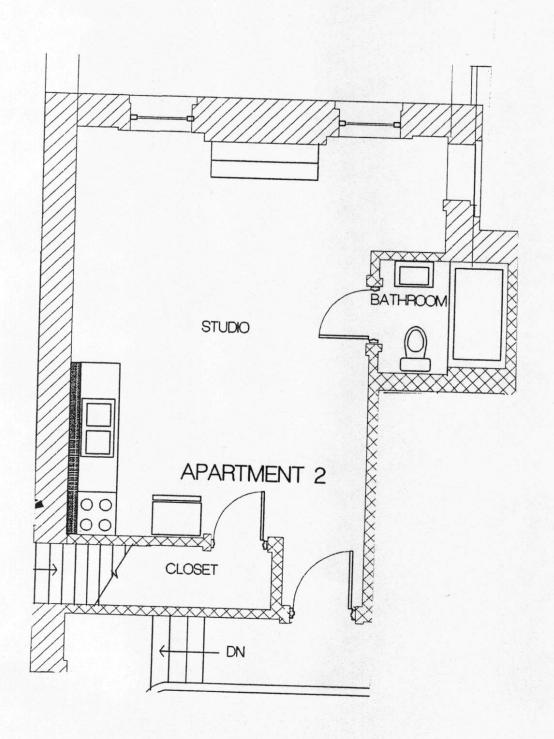


805 OHIO
Apartment 3 – One Bedroom
Second Floor North

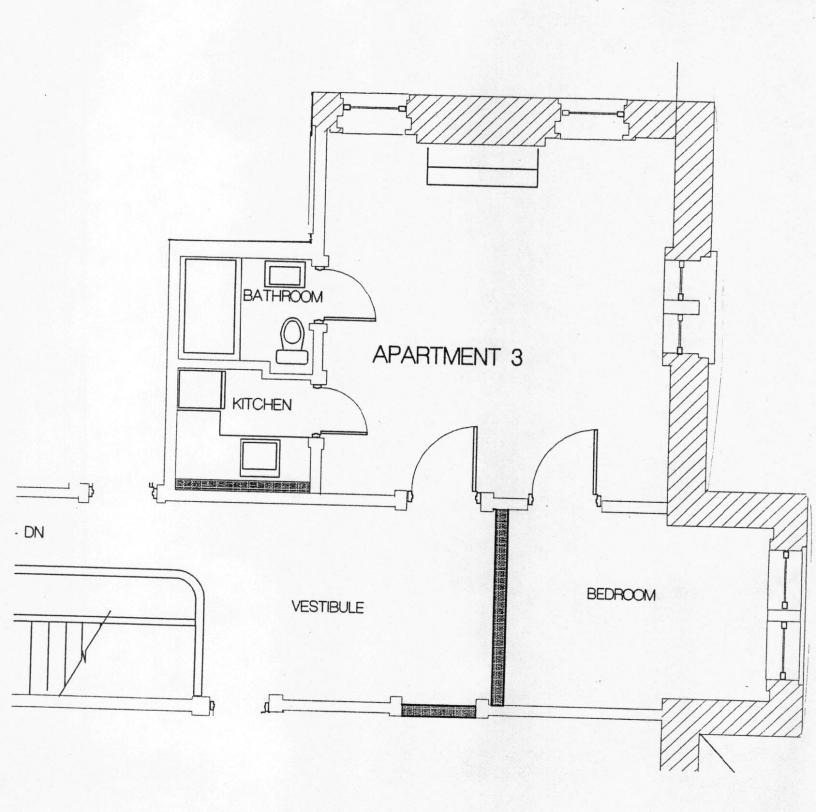

805 OHIO
Apartment 4 – One Bedroom
Second Floor South

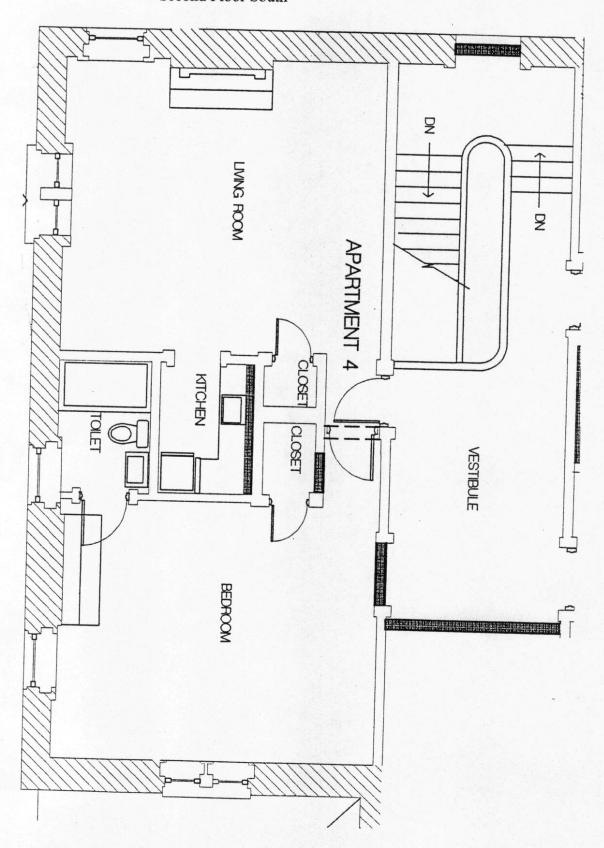

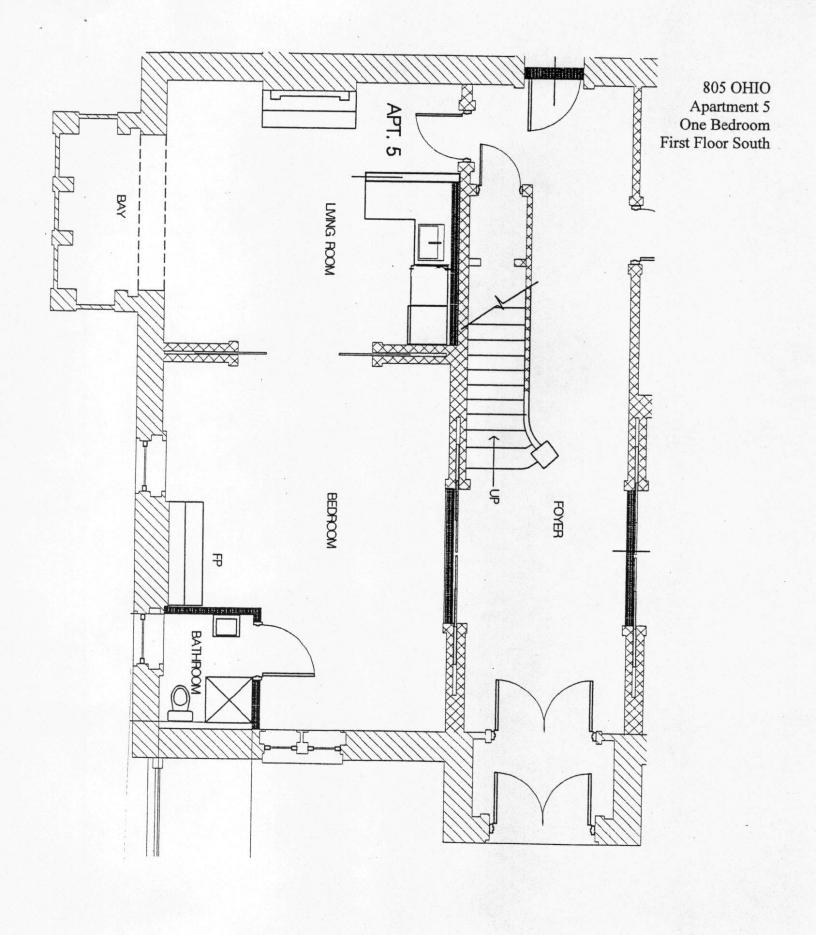





THE FINKBINE MANSION OFFICE BUILDING 1915 Grand Avenue Des Moines, Iowa





INVESTORS MANAGEMENT GROUP OFFICE BUILDING $20^{\rm th}$ and Grand Avenue Des Moines, Iowa
